NAPERVILLE .750 MGL HYDROPILLAR WEST SOUTH WEST EXTERIOR REPAINTING

CITY OF NAPERVILLE , IL
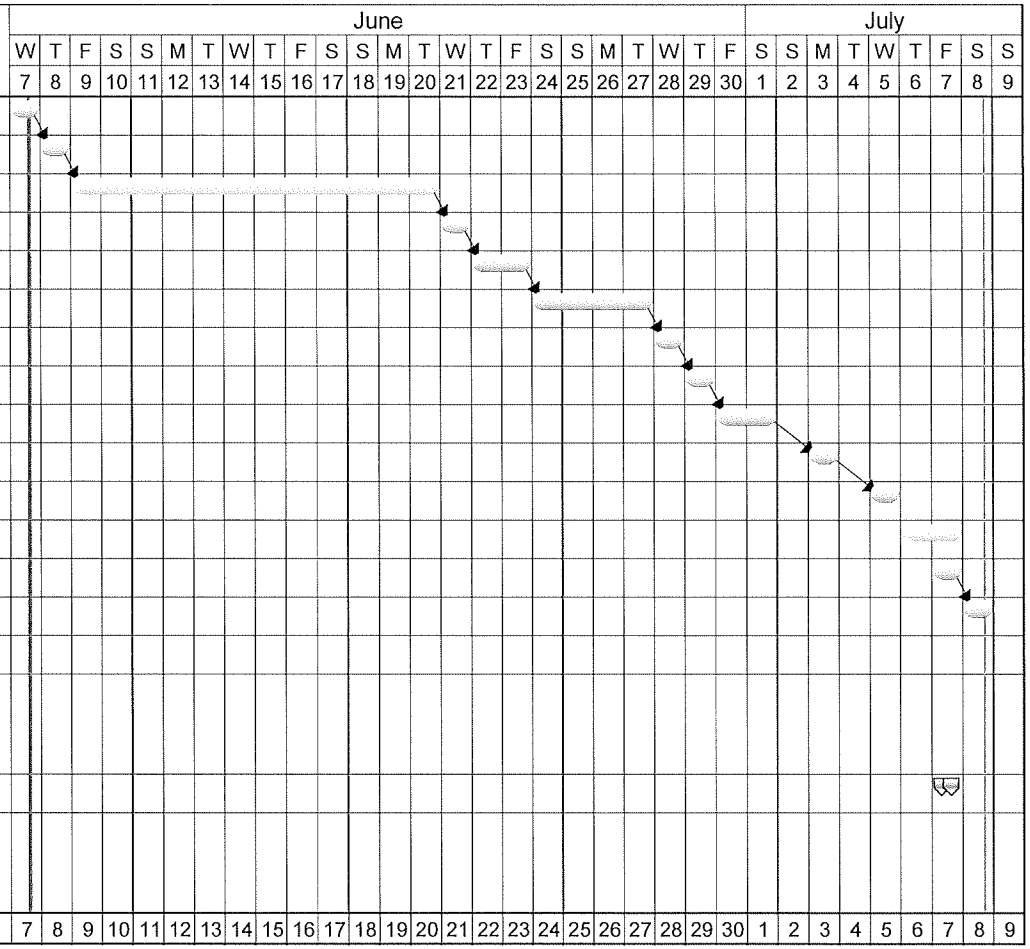
	Activity Name	Duration (Days)	Start Date	Finish Date
1	Notice to Proceed	1.00	6/7/23	6/7/23
2	Reset Abrasive Equip.	1.00	6/8/23	6/8/23
3	Extr. Tank Abrasive/Primer	10.00	6/9/23	6/20/23
4	Extr. Tank Interm/ Stripe	1.00	6/21/23	6/21/23
5	Extr. Interm Urethane	2.00	6/22/23	6/23/23
6	Extr. Fluorl Poly Finish	3.00	6/24/23	6/27/23
7	Extr. T/Up Rigging	1.00	6/28/23	6/28/23
8	Extr. Spot/Finish	1.00	6/29/23	6/29/23
9	LOGO and Lettering	2.00	6/30/23	7/1/23
10	Removal of Waste	1.00	7/3/23	7/3/23
11	Tank Chlorination	1.00	7/5/23	7/5/23
12	Water Sampling/Testing	2.00	7/6/23	7/7/23
13	Punch List/Restoration	1.00	7/7/23	7/7/23
14	Demobilize	1.00	7/8/23	7/8/23
15				
16	EVC Crew will work six days a week and Sundays only if needed.			
17	**Tank In Service**	1.00	7/7/23	7/7/23
18	**PROPOSED SCHEDULE IS WEATHER CONT.**
