

CONTRACT CHANGE ORDER FORM
CHANGE ORDER # 01& P

Project: **2024 Trip Hazard Removal Program - Fall**
Contractor: **ASTI Sawing Inc**
7454 US Hwy 18-151
City, State Zip
CIP No: **MP-004**

Date: **1/31/2025**

Bid/RFP No.: **24-067**
MUNIS No.: **3627**

Change Order Justification:

The amount of this change order exceeds the original contract amount by \$49,296.00 and by 43 days. The revised completion date shall be July 15, 2025.

This change order balances all work completed to date in Areas 1A, 1, and 2 (+484.827 in-ft). These areas were subject to an interim completion date of November 1, 2024.

This change order adds Area 2A - Winding Creek / Maplebrook Extension (+1,438.645 in-ft). A resident called in over 300 locations within this area for sidewalk inspection in the fall of 2024. Due to density of requests received, staff directed the Contractor to begin trip hazard removals in this area to minimize locations which would trigger removal and replacement. This change order pays for work completed to date within this area. The area was not able to be completed through this contract. Staff is evaluating including remaining area on a future trip hazard removal project.

Finally, this change order modifies quantity available to Areas 4, 5, and 6 based on cut rates seen on this program to date. (+1,196.528 in-ft) These additional quantities should allow the remaining areas to be fully improved without need for further change orders.

I, Chris Nichols, of Transportation, Engineering and Development, certify that this work is necessary for successful completion of this work/project/contract. I further certify that: the circumstances said to necessitate the change in performance were not reasonably foreseeable at the time the contract was signed, or the change is germane to the original contract as signed, or the change order is in the best interest of the City and authorized by law.

Account Number	Project Number	Work Order #	Dollar Amount
30282200-551502	MP-004		\$49,296.00

Contract		Authorized Contingency	Days	Dollars
Original Contract	\$103,490.00	Original Amount		\$5,174.50
Prior Cumulative Changes	\$0.00	(-)Previously Authorized		\$0.00
Subtotal	\$103,490.00	Subtotal		\$5,174.50
(+) This Change	\$49,296.00	(-) This Change	43	\$49,296.00
Total Contract	\$152,786.00	Balance Left		\$5,174.50

Note: Needs CC Approval


Engineering Manager/Deputy City Engineer

2/3/2025
Date ChangeOrder01-Cover

CITY OF NAPERVILLE
DEPARTMENT OF TRANSPORTATION & ENGINEERING
AUTHORIZATION OF CONTRACT CHANGES

- ☒ Involving Change in Length of Section or Design
☐ Not Involving Change in Length of Section or Design

To: Mr. David Sollie
Contractor: **ASTI Sawing Inc**
Address: **7454 US Hwy 18-151**
Barneveld, WI 53507

Bid No.: **24-067**
MUNIS No.: **3627**
Project: **2024 Trip Hazard Removal**
Program - Fall

County: DuPage/Will
Section #: 0


CIP No.: **MP-004**
Date: **1/31/2025**

Authorization No.: 01& P

The following change from the plans in the construction of the above designated section of highway improvement is authorized and directed. The estimated quantities are shown below at the awarded contract unit prices except where indicated. The first addition of an item not in the original contract under the fund type or county is indicated by an asterisk (*).


ITEM NO	*	ITEM DESCRIPTION AND UNIT	QUANTITY	UNIT PRICE	ADDITION	DEDUCTION
1		SIDEWALK TRIP HAZARD REMOVAL IN-FT	3,120.00	\$15.80	\$49,296.00	
2						
3						
4						
5						
6						
7						
8						
9						
10						
11						
12						
13						
14						
15						
Amount of original contract :				Totals	\$49,296.00	\$0.00
Net change to date \$49,296.00; % of contract price = 47.6%				Net Change	\$49,296.00	

Signed


Construction Engineering Inspector

2-3-25
Date

Signed


Project Engineer

2/3/25
Date

Approved


Engineering Manager/Deputy City Engineer

2/23/2025
Date

CHANGE ORDER 01 & P

Sidewalk Trip Hazard Removal Construction List

The table below show the locations for the upcoming years program and future programs where sidewalk sawing will be performed to remove trip hazards of 0.25 - 1.5 inches.

Area	Description	Street	Side of Street	Start	End	Road Length	Sidewalk Length (ft)	Sidewalk Length (mi)	ESTIMATE	AS BUILT
1A	Naper Bl	Naper Blvd	Both	Hobson Rd	75th St	1673	3188	0.60	106,855	106,855
1A	Naper Bl	Market Av (E)	North	Naper Blvd	1 property		102	0.02	9,469	9,469
1A	Naper Bl	Market Av (E)	South	Naper Blvd	1 property		55	0.01	6,907	6,907
1A	Naper Bl	Market Av (W)	North	Naper Blvd	1 property		515	0.10	27,097	27,097
1A	Naper Bl	Market Av (W)	South	Naper Blvd	1 property		560	0.11	39,691	39,691
1	Naper Bl	Naper Blvd 1	Both	75th St	Bailey Rd	3340	6411	1.21	415,214	415,214
1	Naper Bl	Heatherfield Cr (N)	Both	Naper Blvd	1 property		392	0.07	10,313	10,313
1	Naper Bl	Brushwood Ct	East	Heatherfield Cr	1 property		103	0.02	9,688	9,688
1	Naper Bl	Bayhill Av	Both	Naper Blvd	1 property		270	0.05	28,158	28,158
1	Naper Bl	Hyde Park Ln	West	Bayhill Av	1 property		203	0.04	28,814	28,814
1	Naper Bl	Heatherfield Cr (S)	Both	Naper Blvd	1 property		363	0.07	0,000	0,000
1	Naper Bl	Sara Ln	Both	Naper Blvd	1 property		190	0.04	24,174	24,174
1	Naper Bl	Harlowe Ct	Both	Naper Blvd	1 property		200	0.04	28,580	28,580
1	Naper Bl	Hyde Park Ln	Both	Naper Blvd	1 property		190	0.04	25,469	25,469
1	Naper Bl	Bakewell Ln	Both	Naper Blvd	1 property		186	0.04	21,143	21,143
1	Naper Bl	Bailey Rd	Both	Naper Blvd	1 property		405	0.08	28,158	28,158
1	Naper Bl	Naper Blvd 2	Both	Bailey Rd	87th St	4860	9627	1.82	565,011	565,011
1	Naper Bl	Timber Trail Dr	Both	Naper Blvd	1 property		225	0.04	39,267	39,267
1	Naper Bl	Shagbark Ct	West	Timber Trail Dr	1 property		101	0.02	8,564	8,564
1	Naper Bl	Orleans Av	Both	Naper Blvd	1 property		395	0.07	33,719	33,719
1	Naper Bl	Amelia Ct	East	Orleans Av	1 property		90	0.02	0,000	0,000
1	Naper Bl	River Oak Dr	Both	Naper Blvd	1 property		319	0.06	22,515	22,515
1	Naper Bl	Winola Ct	Both	River Oak Dr	1 property		181	0.03	0,000	0,000
1	Naper Bl	Ursuline Av	Both	Naper Blvd	1 property		261	0.05	10,938	10,938
1	Naper Bl	Elyse Ln	East	Ursuline Av	1 property		170	0.03	22,344	22,344
1	Naper Bl	Carriage Hill Rd	Both	Naper Blvd	1 property		196	0.04	34,190	34,190
1	Naper Bl	Scott School	-	Naper Blvd	Warwick Dr		415	0.08	2,500	2,500
1	Naper Bl	Warwick Dr	East	School property	School property		1059	0.20	69,255	69,255
1	Naper Bl	Stoney Brook Dr	Both	Naper Blvd	1 property		242	0.05	10,938	10,938
1	Naper Bl	Lakeview Ct	West	Stoney Brook Dr	1 property		138	0.03	21,345	21,345
1	Naper Bl	Staunton Rd	Both	Naper Blvd	1 property		233	0.04	15,251	15,251
1	Naper Bl	Spindletree Av	Both	Naper Blvd	1 property		332	0.06	22,219	22,219
1	Naper Bl	87th St	North	Naper Blvd	1 property		226	0.04	12,438	12,438
1	Naper Bl	Debbie Ct	West	87th St	1 property		159	0.03	7,001	7,001

CHANGE ORDER 01 & P

Sidewalk Trip Hazard Removal Construction List

The table below show the locations for the upcoming years program and future programs where sidewalk sawing will be performed to remove trip hazards of 0.25 - 1.5 inches.

Area	Description	Street	Side of Street	Start	End	Road Length	Sidewalk Length (ft)	Sidewalk Length (mi)	ESTIMATE	AS BUILT
2a	Winding Creek/Maple	Terrance Dr 1	Both	Prairie Knoll Dr	130' N of Quail Dr	1696	3141	0.59		
2a	Winding Creek/Maple	Terrance Dr 2	Both	130' N of Quail Dr	Winding Creek Dr	2666	5052	0.96		
2a	Winding Creek/Maple	Terrance Dr 3	Both	Winding Creek Dr	Waxwing Av	360	627	0.12		
2a	Winding Creek/Maple	Waxwing Av	South	Terrance Dr	1 property	-	262	0.05		
2a	Winding Creek/Maple	Bethany Ct	Both	Terminus	Terrance Dr	460	998	0.19		
2a	Winding Creek/Maple	Winding Creek Dr	Both	Terrance Dr	Bailey Rd	2363	4541	0.86		
2a	Winding Creek/Maple	Meander Dr	Both	Bailey Rd	Winding Creek Dr	1025	1933	0.37		
2a	Winding Creek/Maple	Woodcreek Ct	Both	Winding Creek Dr	Terminus	118	381	0.07		
2a	Winding Creek/Maple	Rill Ct	Both	Winding Creek Dr	Terminus	240	570	0.11		
2a	Winding Creek/Maple	Stone Creek Ct	Both	Terminus	Winding Creek Dr	220	520	0.10		
2a	Winding Creek/Maple	Fall Creek Ct	Both	Bailey Rd	Terminus	213	494	0.09		
2a	Winding Creek/Maple	Bailey Rd 1	Both	Modaff Dr	500' E Winding Creek	3310	5770	1.09		
2a	Winding Creek/Maple	Modaff Rd	East	Bailey Rd	1 property		216	0.04		
2a	Winding Creek/Maple	Bailey Rd 2	Both	500' E Winding Creek	Washington St	2607	4629	0.88	292.760	292.760
2a	Winding Creek/Maple	Washington St	West	Bailey Rd	1 property		189	0.04	17.876	17.876
2a	Winding Creek/Maple	Flock Av 1	Both	Terrance Dr	Bailey Rd (W)	2528	4912	0.93		
2a	Winding Creek/Maple	Flock Av 2	Both	Bailey Rd (W)	Bailey Rd (E)	1574	3178	0.60		
2a	Winding Creek/Maple	Cascade Ct	Both	Terminus	Terminus	669	1438	0.27		
2a	Winding Creek/Maple	Rapids Ct	Both	Bailey Rd	Terminus	161	408	0.08		
2a	Winding Creek/Maple	Estuary Ct	Both	Terminus	Flock Av	145	381	0.07		
2a	Winding Creek/Maple	Riparian Dr 1	Both	Prairie Knoll Dr	120' N of Quail Dr	1663	3091	0.59		
2a	Winding Creek/Maple	Riparian Dr 2	Both	120' N of Quail Dr	Bailey Rd	1023	2075	0.39		
2a	Winding Creek/Maple	Placer Ct	Both	Terminus	Terrance Dr	851	1791	0.34		
2a	Winding Creek/Maple	Prairie Knoll Dr	Both	Redstart Rd	81st St	4629	9167	1.74		
2a	Winding Creek/Maple	Delkir Ct	Both	Prairie Knoll Dr	Terminus	576	1249	0.24		
2a	Winding Creek/Maple	Cloverleaf Ct	Both	Prairie Knoll Dr	Terminus	582	1254	0.24		
2a	Winding Creek/Maple	Peacock Ct	Both	Quail Dr	Terminus	598	1255	0.24		
2a	Winding Creek/Maple	Quail Dr	Both	81st St	Terrance Dr	2313	4576	0.87		
2a	Winding Creek/Maple	81st St	Both	Modaff Rd	Dr	199	309	0.06		
2a	Winding Creek/Maple	Modaff Rd	East	81st St	1 property		204	0.04		
2a	Winding Creek/Maple	Northfield Dr	Both	Cedarbrook Rd	Prairie Knoll Dr	326	526	0.10		
2a	Winding Creek/Maple	Cedarbrook Rd	North	Northfield	1 property		194	0.04		
2a	Winding Creek/Maple	Redstart Rd 1	Both	Riparian Dr	140' E of Prairie Knoll	1823	3276	0.62		
2a	Winding Creek/Maple	Redstart Rd 2	Both	140' E of Prairie Knoll	Washington St	2423	5167	0.98	299.162	299.162
2a	Winding Creek/Maple	Washington St	West	Redstart Rd	1 property		251	0.05		
2a	Winding Creek/Maple	Ceals Ct	Both	Terminus	Redstart Rd	517	1104	0.21		
2a	Winding Creek/Maple	Welton Ct	Both	Terminus	Redstart Rd	526	1121	0.21		
2a	Winding Creek/Maple	Sagebrush Rd	Both	Riparian Dr	Terrance Dr	918	1767	0.33		
2a	Winding Creek/Maple	Clyde Dr 1	Both	155' N of Foxcroft Rd	Bailey Rd	2773	5265	1.00		
2a	Winding Creek/Maple	Clyde Dr 2	Both	Bailey Rd	1 property north		234	0.04		
2a	Winding Creek/Maple	Verdin Ln	Both	Clyde Dr	Bailey Rd	933	1815	0.34		
2a	Winding Creek/Maple	Drendel Ln	Both	Clyde Dr	Killdeer Rd	1157	2192	0.42		

CHANGE ORDER 01 & P


Sidewalk Trip Hazard Removal Construction List

The table below show the locations for the upcoming years program and future programs where sidewalk sawing will be performed to remove trip hazards of 0.25 - 1.5 inches.

Area	Description	Street	Side of Street	Start	End	Road Length	Sidewalk Length (ft)	Sidewalk Length (mi)	ESTIMATE	AS BUILT
4	Lakewood	Fort Hill Dr 4	Both	Ogden Av	Sanctuary Ln	1357	2840	0.54	170,000	
4	Lakewood	Lexington Ln	Both	Fort Hill Dr	1 property		406	0.08	25,000	
4	Lakewood	Emerson Ln	West	Lexington Ln	1 property		82	0.02	7,000	
4	Lakewood	John Friend Dr	Both	Fort Hill Dr	1 property		143	0.03	11,000	
4	Lakewood	Sanctuary Ln	Both	Fort Hill Dr	1 property		941	0.18	57,000	
4	Lakewood	John Friend Dr	West	Sanctuary Ln	School property		440	0.08	28,000	
4	Lakewood	Fort Hill Dr 5	Both	Sanctuary Ln	Three Farms Av	1488	2563	0.49	155,000	
4	Lakewood	Blakely Ln	Both	Fort Hill Dr	1 property		148	0.03	11,000	
4	Lakewood	Fairbanks Ct	Both	Fort Hill Dr	1 property		156	0.03	11,000	
4	Lakewood	Dunraven Av	Both	Fort Hill Dr	1 property		195	0.04	13,000	
4	Lakewood	Audrey Av	Both	Fort Hill Dr	1 property		815	0.15	50,000	
4	Lakewood	Three Farms Av	Both	Fort Hill Dr	1 property		654	0.12	40,000	
4	Lakewood	Fort Hill Dr 6	East	Three Farms Av	75th St	406	420	0.08	25,000	
4	Lakewood	Crossing Ct	Both	Three Farms Av	Terminus	359	875	0.17	55,000	
4	Lakewood	Three Farms Av	South	Crossing Ct	1 property		258	0.05	17,000	
4	Lakewood	Hannah Ct	Both	Terminus	Three Farms Av	140	454	0.09	30,000	
4	Lakewood	Three Farms Av	North	Hannah Ct	1 property		183	0.03	13,000	
4	Lakewood	Andria Ct	Both	Three Farms Av	Terminus	230	618	0.12	40,000	
4	Lakewood	Three Farms Av	South	Andria Ct	1 property		220	0.04	15,000	
4	Lakewood	Mallory Ct	Both	Terminus	Three Farms Av	133	441	0.08	30,000	
4	Lakewood	Three Farms Av	North	Mallory Ct	1 property		228	0.04	15,000	
4	Lakewood	Natalie Ct	Both	Terminus	Three Farms Av	191	543	0.10	35,000	
4	Lakewood	Three Farms Av	North	Natalie Ct	1 property		189	0.04	13,000	
4	Lakewood	Samuel Ct	Both	Three Farms Av	Terminus	197	555	0.11	35,000	
4	Lakewood	Three Farms Av	South	Samuel Ct	1 property		213	0.04	15,000	
4	Lakewood	Jessica Ct	Both	Lakewood Cr	Terminus	172	511	0.10	35,000	
4	Lakewood	Lakewood Cr	East	Jessica Ct	1 property		210	0.04	13,000	
4	Lakewood	Meagan Ct	Both	Sanctuary Ln	Terminus	355	852	0.16	55,000	
4	Lakewood	Sanctuary Ln	South	Meagan Ct	1 property		206	0.04	13,000	
4	Lakewood	Matthew Ct	Both	Terminus	Sanctuary Ln	425	987	0.19	65,000	
4	Lakewood	Sanctuary Ln	North	Matthew Ct	1 property		237	0.04	15,000	
4	Lakewood	Chang Ct	Both	Schumacher Ln	Terminus	213	593	0.11	40,000	
4	Lakewood	Schumacher Ln	East	Chang Ct	1 property		210	0.04	13,000	
4	Lakewood	Joan Ct	Both	Terminus	Sanctuary Ln	118	395	0.07	25,000	
4	Lakewood	Sanctuary Ln	North	Joan Ct	1 property		262	0.05	17,000	
4	Lakewood	Book Rd 8	Both	75th St	Rickert Dr	1150	2198	0.42	135,000	
4	Lakewood	Three Farms Av	Both	Book Rd	1 property		425	0.08	28,000	
4	Lakewood	Crossing Ln	East	Three Farms Av	1 property		68	0.01	5,000	

City of Naperville
2024 Trip Hazard Removal Program (Fall)

Project Overview

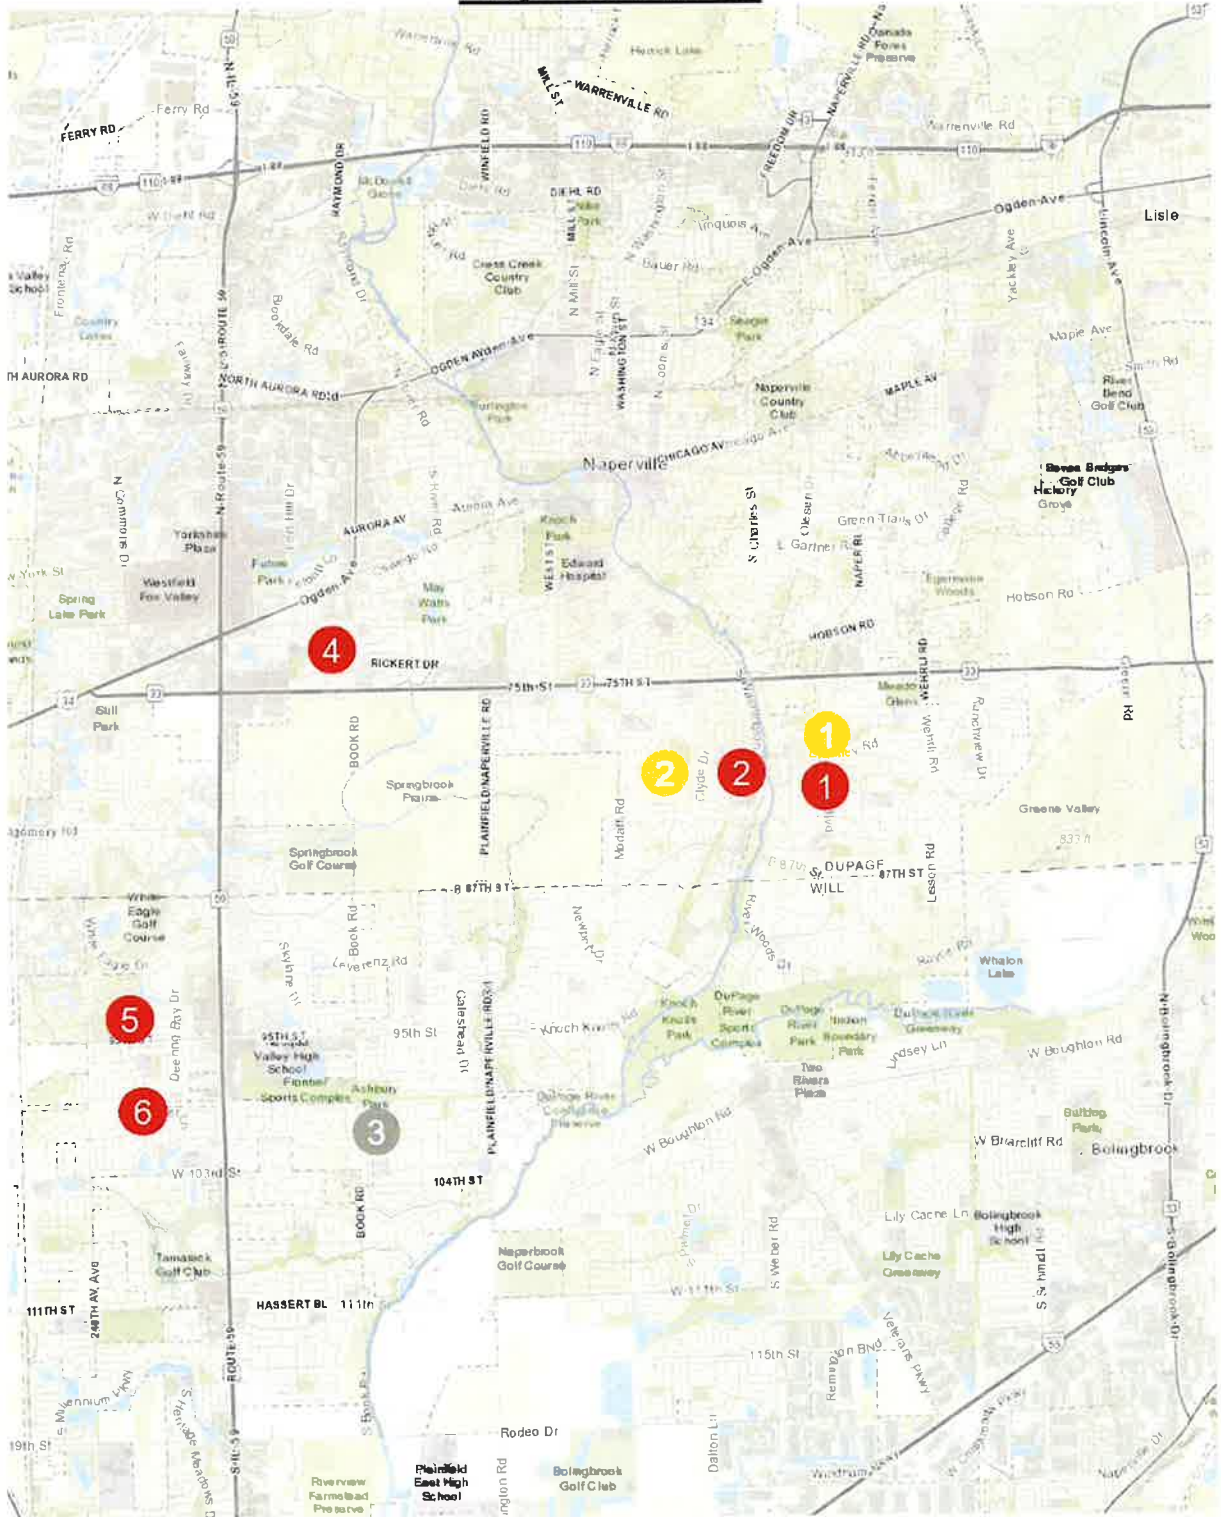


Area 1 – Naper Blvd




- Both sides of street
- One side of street

Area 4 – Lakewood

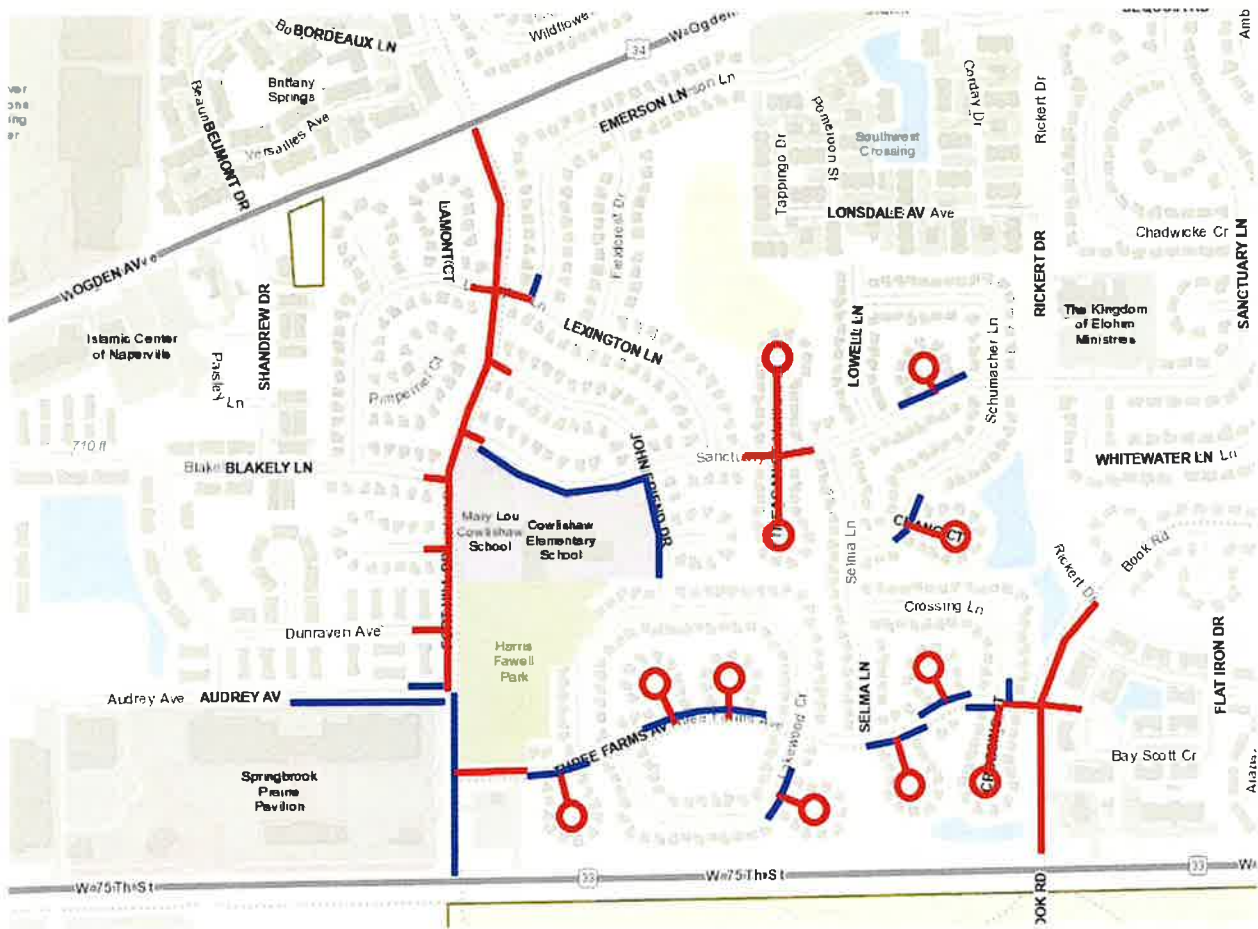

- Both sides of street
- One side of street

Area 6 – Tall Grass

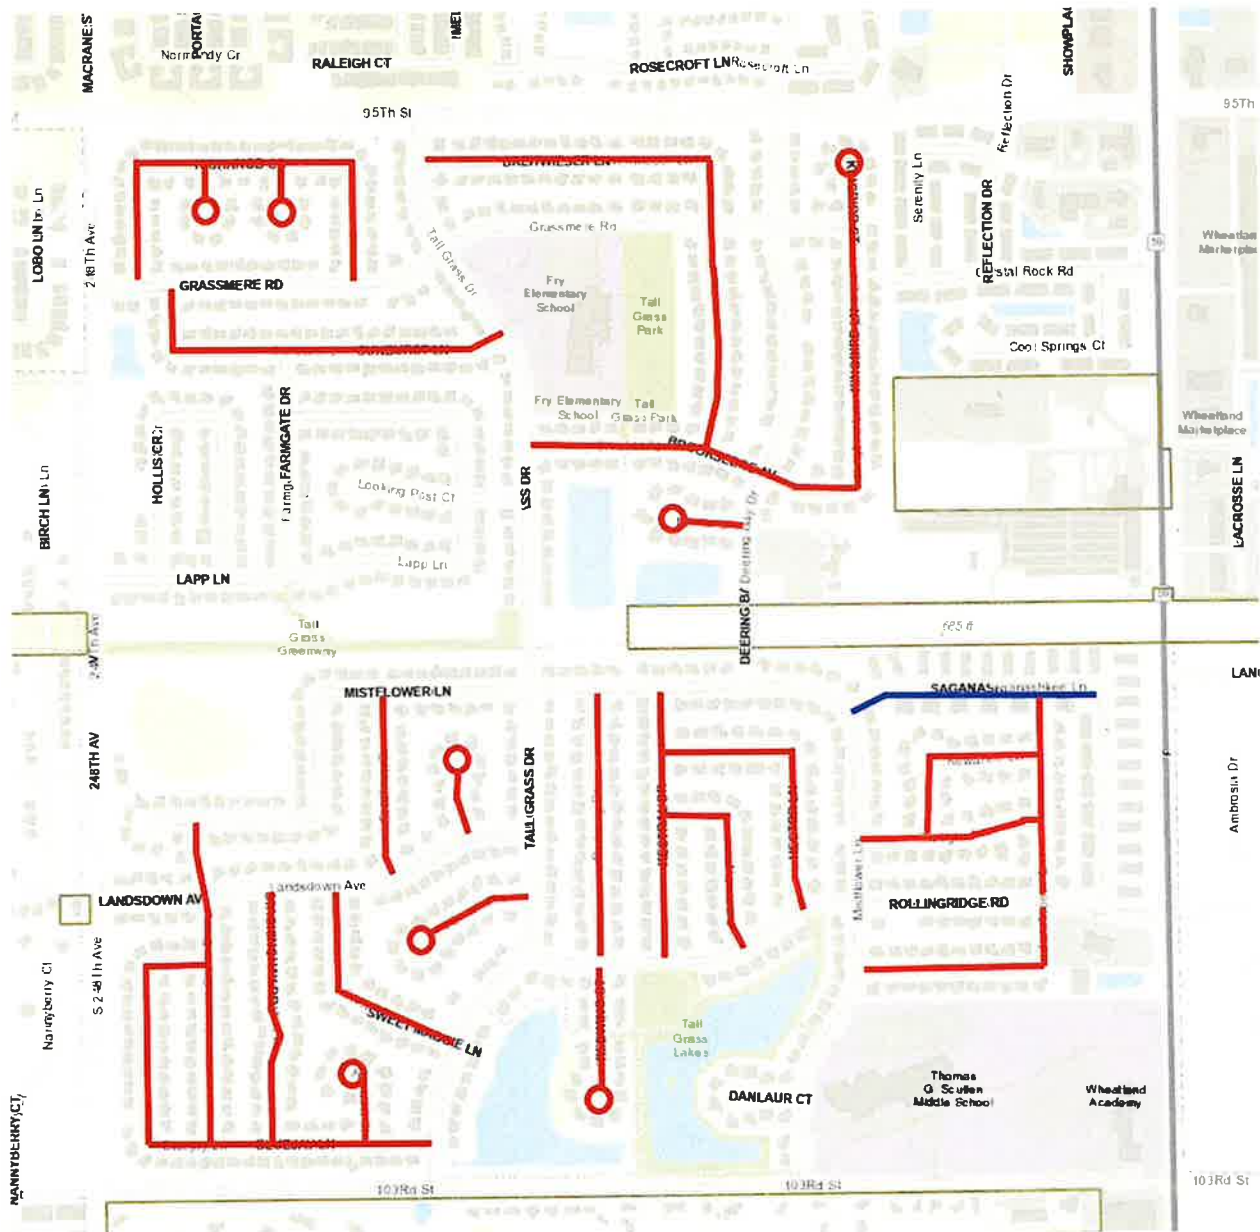

-  Both sides of street
 One side of street
